


	<b>Environment Clearance Compliance Report</b>		
Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

**ENVIRONMENT CLEARANCE (EC) COMPLIANCE REPORT.**

**CIDCO – PMAY Package – ii Project.**

**Project Location: Vashi Truck Terminal (VTT)**

**Date: 10.06.2023**



	<b>Environment Clearance Compliance Report</b>		
Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

There are Two types of condition for Environment Clearance.

1. SPECIFIC CONDITION.
2. GENERAL CONDITION.

**SPECIFIC CONDITION**

Sr. No	Description	Remarks
1	PP to upload the disaster management plan considering the failure of mitigation measures provided by them like effluent treatment plant, grease traps, Air cleaning system, noise barriers etc. as one of the likely disaster point.	NA
2	PP to reuse the treated water for bus cleaning. Also to provide water treatment plant in project site itself.	NA at this stage as construction is progress.
3	The PP to get NOC from competent authority with reference to Thane creek flamingo sanctuary if the project site falls within 10 Km radius from the said sanctuary boundary. The planning authority to ensure fulfilment of this condition before granting CC.	Not Applicable
4	PP to ensure that CER plan get approved from Municipal Commissioner/District Collector.	Noted
5	PP Shall comply with Standard EC conditions mentioned in the Office Memorandum issued by MoEF& CC vide F.No.22-34/20 18-IA.111 dt.04.0 1.2019.	Noted
6	SEIAA decided to grant EC for-FSI-57748.80 m2, Non-FSI- 69516.50 m2 and Total BUA-127265.30 m2 (Plan Approval no- CIDCO/Sr. Arch.(BP-IHP)/2019/365, Date 08.08.20 19)	For Information.

	<b>Environment Clearance Compliance Report</b>		
Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

**GENERAL CONDITION.**

Sr. No	Description	Remarks
1	E-waste shall be disposed through Authorized vendor as per E-waste (Management and Handling) Rules, 2016.	Shall be comply at the time of generation
2	The Occupancy Certificate shall be issued by the Local Planning Authority to the project only after ensuring sustained availability of drinking water, connectivity of sewer line to the project site and proper disposal of treated water as per environmental norms.	Post Construction stage.
3	This environmental clearance is issued subject to obtaining NOC from Forestry & Wild life angle including clearance from the standing committee of the National Board for Wild life as if applicable & this environment clearance does not necessarily implies that Forestry & Wild life clearance granted to the project which will be considered separately on merit.	Not Applicable
4	PP has to abide by the conditions stipulated by SEAC& SEIAA.	Noted
5	The height, Construction built up area of proposed construction shall be in accordance with the existing FSI/FAR norms of the urban local body & it should ensure the same along with survey number before approving layout plan & before according commencement certificate to proposed work. Plan approving authority should also ensure the zoning permissibility for the proposed project as per the approved development plan of the area.	CC received from concern authority.
6	If applicable Consent for Establishment" shall be obtained from Maharashtra Pollution Control Board under Air and Water Act and a copy shall be submitted to the Environment department before start of any construction work at the site.	CTE granted by MPCB
7	All required sanitary and hygienic measures should be in place before starting construction activities and to be maintained throughout the construction phase.	Necessary measures in place. Refer Annexure - <b>01</b>
8	Adequate drinking water and sanitary facilities should be provided for construction workers at the site. Provision should be made for mobile toilets. The safe disposal of wastewater and solid wastes generated during the construction phase should be ensured.	Adequate provision made / provided. Refer Annexure - <b>02</b>
9	The solid waste generated should be properly collected and segregated. Dry/inert solid waste should be disposed of to the approved sites for land filling after recovering recyclable material.	Solid waste collected at designated place and dispose of through authorise vendor
10	Disposal of muck during construction phase should not create any adverse effect on the neighboring communities and be disposed taking the necessary precautions for general safety and health aspects of people, only in approved sites with the approval of competent authority.	Muck dispose of in designated place / plot.
11	Arrangement shall be made that waste water and storm water do not get mixed.	Noted
12	All the topsoil excavated during construction activities should be stored for use in horticulture / landscape development within the project site.	Followed. Refer Annexure - <b>03</b>
13	Additional soil for levelling of the proposed site shall be generated within the sites (to the extent possible) so that natural drainage system of the area is protected and improved.	Noted
14	Green Belt Development shall be carried out considering CPCB guidelines including selection of plant species and in consultation with the local DFO/ Agriculture Dept.	Noted. Will take action completion of building work.

Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

15	Soil and ground water samples will be tested to ascertain that there is no threat to ground water quality by leaching of heavy metals and other toxic contaminants.	Tests are conducted and reports enclosed. Refer Annexure - <b>04</b>
16	Construction spoils, including bituminous material and other hazardous materials must not be allowed to contaminate watercourses and the dumpsites for such material must be secured so that they should not leach into the ground water.	Construction Spoils and other hazardous material collect and dispose off in proper way to avoid water contamination. Refer Annexure - <b>05</b>
17	Any hazardous waste generated during construction phase should be disposed of as per applicable rules and norms with necessary approvals of the Maharashtra Pollution Control Board.	Noted
18	The diesel generator sets to be used during construction phase should be low Sulphur diesel type and should conform to Environments (Protection) Rules prescribed for air and noise emission standards.	Followed, Record enclosed. Refer Annexure - <b>06</b>
19	The diesel required for operating DG sets shall be stored in underground tanks and if required, clearance from concern authority shall be taken.	Only 400 Ltr. Store which is less than permissible limit.
20	Vehicles hired for bringing construction material to the site should be in good condition and should have a pollution check certificate and should conform to applicable air and noise emission standards and should be operated only during non-peak hours.	Complied, Refer Annexure - <b>07</b>
21	Ambient noise levels should conform to residential standards both during day and night. Incremental pollution loads on the ambient air and noise quality should be closely monitored during construction phase. Adequate measures should be made to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards by CPCB/MPCB.	Followed. Refer Annexure - <b>08</b>
22	Fly ash should be used as building material in the construction as per the provisions of Fly Ash Notification of September 1999 and amended as on 27th August, 2003. (The above condition is applicable only if the project site is located within the 100Km of Thermal Power Stations).	Fly ash as well as GGBS use in works.
23	Ready mixed concrete must be used in building construction.	Complied
24	Storm water control and its re-use as per CGWB and <b>BIS</b> standards for various applications.	Not Applicable
25	Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.	Curing Compound used to reduce the water demand during construction. Refer Annexure - <b>09</b>
26	The ground water level and its quality should be monitored regularly in consultation with Ground Water Authority.	Ground water quality test has been undertaken and recorded.
27	The installation of the Sewage Treatment Plant (STP) should be certified by an independent expert and a report in this regard should be submitted to the <b>MPCB</b> and Environment department before the project is commissioned for operation. Discharge of this unused treated effluent, if any should be discharge in the sewer line. Treated effluent emanating from STP shall be recycled/ refused to the maximum extent possible. Discharge of this unused treated effluent, if any should be discharge in the sewer line. Treatment of 100% grey water by decentralized treatment should be done. Necessary measures should be made to mitigate the odour problem from STP.	Noted
28	Permission to draw ground water and construction of basement if any shall be obtained from the competent Authority prior to construction/operation of the project.	No basement in project and ground water not being use for construction

Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

29	Separation of grey and black water should be done by the use of dual plumbing line for separation of grey and black water.	Included, will be taken up on commencement of work.
30	Fixtures for showers, toilet flushing and drinking should be of low flow either by use of aerators or pressure reducing devices or sensor based control.	Material selection is in process & considered by accordingly.
31	Use of glass may be reduced up to 40% to reduce the electricity consumption and load on air conditioning. If necessary, use high quality double glass with special reflective coating in windows.	Not Applicable
32	Roof should meet prescriptive requirement as per Energy Conservation Building Code by using appropriate thermal insulation material to fulfil requirement.	Noted
33	Energy conservation measures like installation of CFLs /TFLs for the lighting the areas outside the building should be integral part of the project design and should be in place before project commissioning. Use CFLs and TFLs should be properly collected and disposed of/sent for recycling as per the prevailing guidelines/rules of the regulatory authority to avoid mercury contamination. Use of solar panels may be done to the extent possible like installing solar street lights, common solar water heaters system. Project proponent should install, after checking feasibility, solar plus hybrid non-conventional energy source as source of energy.	Included, will be taken up on commencement of work.
34	Diesel power generating sets proposed as source of backup power for elevators and common area illumination during operation phase should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The height of stack of DG sets should be equal to the height needed for the combined capacity of all proposed DG sets. Use low Sulphur diesel. The location of the DG sets may be decided with in consultation with Maharashtra Pollution Control Board.	Noted
35	Noise should be controlled to ensure that it does not exceed the prescribed standards. During nighttime the noise levels measured at the boundary of the building shall be restricted to the permissible levels to comply with the prevalent regulations.	Followed Noise Monitoring report enclosed. Refer Annexure - 10
36	Traffic congestion near the entry and exit points from the roads adjoining the proposed project site must be avoided. Parking should be fully internalized and no public space should be utilized.	Followed. Refer Annexure - 11
37	Opaque wall should meet prescriptive requirement as per Energy Conservation Building Code, which is proposed to be mandatory for all air-conditioned spaces while it is aspiration for non-air conditioned spaces by use of appropriate thermal insulation material to fulfil requirement.	Not Applicable.
38	The building should have adequate distance between them to allow movement of fresh air and passage of natural light, air and ventilation.	Provided
39	Regular supervision of the above and other measures for monitoring should be in place all through the construction phase, so as to avoid disturbance to the surroundings.	Regular supervision for monitoring of applicable provision/measures in place.
40	Under the provisions of Environment (Protection) Act, 1986, legal action shall be initiated against the project proponent if it was found that construction of the project has been started without obtaining environmental clearance.	Work started after obtaining EC and other statutory approval.
41	Six monthly monitoring reports should be submitted to the Regional office MoEF, Bhopal with copy to this department and MPCB.	Followed.

Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

42	Project proponent shall ensure completion of SIP, MSW disposal facility, green belt development prior to occupation of the buildings. As agreed during the SEIAA meeting, PP to explore possibility of utilizing excess treated water in the adjacent area for gardening before discharging it into sewer line No physical occupation or allotment will be given unless all above said environmental infrastructure is installed and made functional including water requirement in Para 2. Prior certification from appropriate authority shall be obtained.	Noted
43	Wet garbage should be treated by Organic Waste Converter and treated waste (manure) should be utilized in the existing premises for gardening. And, no wet garbage will be disposed outside the premises. Local authority should ensure this.	Noted
44	Local body should ensure that no occupation certification is issued prior to operation of STP/MSW site etc. with due permission of MPCB.	Noted
45	A complete set of all the documents submitted to Department should be forwarded to the Local authority and MPCB.	Submitted.
46	In the case of any change(s) in the scope of the project. the project would require a fresh appraisal by this Department.	Noted
47	A separate environment management cell with qualified staff shall be set up for implementation of the stipulated environmental safeguards.	Noted
48	Separate funds shall be allocated for implementation of environmental protection measures/EMP along with item-wise breaks-up. These cost shall be included as part of the project cost. The funds earmarked for the environment protection measures shall not be diverted for other purposes and year wise expenditure should reported to the MPCB & this department.	Noted
49	The project management shall advertise at least in two local newspapers widely circulated in the region around the project, one of which shall be in the Marathi language of the local concerned within seven days of issue of this letter, informing that the project has been accorded environmental clearance and copies of clearance letter are available with the Maharashtra Pollution Control Board and may also be seen at Website at <a href="http://parivesh.nic.in">http://parivesh.nic.in</a>	Noted
50	Project management should submit half yearly compliance reports in respect of the stipulated prior environment clearance terms and conditions in hard & soft copies to the MPCB & this department, on 1st June & 1 st December of each calendar year.	Submitted
51	A copy of the clearance letter shall be sent by proponent to the concerned Municipal Corporation and the local NGO, if any, from whom suggestions/representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the Company by the proponent.	Noted
52	The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; <b>SPM, RSPM</b> . SO <sub>2</sub> , NO <sub>x</sub> (ambient levels as well as stack emissions) or critical sector parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.	Noted
53	The project proponent shall also submit six monthly reports on the status of compliance of the stipulated EC conditions including results of monitored	Submitted

Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

	data (both in hard copies as well as by e-mail) to the respective Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB.	
54	The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions a shall also be sent to the respective Regional Offices of MoEF by e-mail.	Submitted

Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

**Annexure- 01** : - All required sanitation and hygienic measures have been taken prior to start the construction work and it shall be maintained till completion of project.





Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

**Annexure – 02 :-** Adequate drinking water and sanitary facilities provided for construction workers at the site.  
The safe disposal of wastewater and solid wastes in place.





RO facility available at site and Workmen Camp for drinking water.

Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

**Annexure: – 03:** All the excavated topsoil stored and used for horticulture / landscape development within the project site.



Excavated top soil stored at site for landscaping and backfilling.

	<b>Environment Clearance Compliance Report</b>		
Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

**Annexure – 04** : Ground water testing is being followed for water quality monitoring.



## INDIAN MATERIAL RESEARCH CENTER

Expert Analyst for Geotechnical/ Geological Investigation, Land and Marine, Surveying work, Concrete, Asphalt, Reinforcement, Cements, MDT and Other Engineering Material  
Email: imrc\_analys@yashwanth.com

Location-1: Plot No. G-75/76, Sector-12, Kharghar, Navi Mumbai - 410210  
Location-2: Shop No. 13, Shiv Chatrapati Mini Market Association, Plot No. G-41, Sec-12, Kharghar, Navi Mumbai - 410210

ISO/IEC 17005 Accredited Testing Laboratory by National Accreditation Board For Testing and Calibration Laboratories (NABL) Vide Certificate Number TC-8222





### TEST REPORT

<b>ULR NO</b>	TCR23225000004914F
Test Report No. & date	IMRC/TR/230520001-1 22-05-2023
Name of Customer & Address Name & Address of Project	M/s. CAPACITE INFRAPROJECTS LTD. Construction of approx. 21346 Nos. of EWS/LIG type dwelling unit (Package-II) with development of commercial area & onsite infrastructure works at various location, viz. Kharghar Bus Terminal, Panel Bus Terminal, Kallamboli Bus Depot, Kharghar Bus Depot, Vashi Truck Terminal & Kharghar Sector-14, Navi Mumbai.
Name of Consultants/Contractor	—
Customer reference no.	CL/IGC/VTT/TR/221 Letter Dated - 20/05/2023
Nature/Source of the Sample	Water for Construction
Quantity of the sample	1 bottle (1000 ml)
Condition of the sample	Acceptable
Date of receipt of sample	20-05-2023
Date of start of analysis	21-05-2023
Date of completion of analysis	21-05-2023

**CHEMICAL TESTING**

**WATER**

Sample tested at : Location 1

Environmental Condition		Humidity	Ambient	Temperature	Ambient
Sr. No.	Test Parameters	Units	Results	Acceptance Criteria As Per: IS-456: 2000: RA 2023	Test Method
1	Sulphate as SO <sub>4</sub>	mg/lit	18.9	400 Max.	IS 3025 P-24 sec-1:2022
2	Chloride as Cl <sub>1</sub>	mg/lit	68.7	2000 mg/lit for concrete not containing embedded steel and 500 mg/lit for reinforced concrete work.	IS 3025 P-32 1988/(RA 2015)
3	pH at 25° C	—	7.46	6.0 Min.	IS 3025 P-11:2022

Remark: "The above samples conforms to IS-456: 2000: RA 2023 specification w.r.t. test carried out when measurement uncertainty is taken in to account."

This test report refers only to the sample submitted for testing.  
Report of tests samples will be preserved with us for two years from the date of testing.  
Any correction invalidates this test report.  
This report shall not be reproduced except in full without written approval from M/s. Indian Material Research Center.

*Johnson*  
-125 Sheela  
12/06/2023

*G. J. J.*  
Gaurav J. J. J.  
12/06/23

*Khambaye*  
Authorized Signatory  
Anuja Khambaye  
HDD - Chemical

END OF REPORT



FORMAT NO : MRC/IM/47/005/006

REV NO : 01



Page 1 of 1

Creating Concrete Bond With Strong Foundation.


Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

**Annexure – 05:** Construction's Spoils and other hazardous material collected and disposed of in proper way to avoid water contamination.



	<b>Environment Clearance Compliance Report</b>		
Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

**Annexure – 06:** The diesel generator's stack monitoring is being followed at site, conform to Environments (Protection) Rules prescribed for air and noise emission standards.



## GREEN CIRCLE, INC.

Integrated HSEQR Consulting Engineers, Scientists & Trainers  
(Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986)  
(No. Q - 1505 / 32 / 2007 - CPW)  
(ISO 9001, 14001 & OHSAS 18001 Certified Organization)

Report No. - GC/VLAB/EM-0012/23-EP/23-23/April - 06/2023 Date: 08/04/23

### ANALYSIS REPORT


(For the month of August)

Client Details		Sample Details	
Name	M/s. Capacite Infraprojects Ltd.	Sample Code	GCIV/22/C1/C2/ST3
Address	G/000 - Vashi Truck Terminal, Near AFMC Market, Sector - 19, Vashi Navi Mumbai - 400703	Location	D.G. Set (250 KVA)
		Sampling Instrument	Stack Monitoring Kit
Sampling Done By	Mr. Vikram	Date of Sampling	03/04/23
Analysis Starts on	05/04/23	Sampling Method	isokinetic Sampling, IS:11255_PART-1,2,3
Analysis Completion On	05/04/23	Sample Received Date	05/04/23

### STACK MONITORING ANALYSIS REPORT

Sr. No.	Parameters	Unit	Results
1.	Type of fuel used	Type	Diesel
2.	Material Of Construction	Type	M.S



Sr.No.	Parameters	Unit	Results	limit as Per CPCB	Reference Method
1.	Particulate Matter (PM)	g/kw-hr	0.038	50.2	IS:11255 (Part 1): 1985
2.	Sulphur Dioxide (SO2)	g/kw-hr	ND	N.S.	IS:11255 (Part 2): 1985
3.	Oxides of Nitrogen (NOx) + HC.	g/kw-hr	0.62	5.0	IS:11255 (Part 7): 2005



Authorized Signatory

- Analysis is subject to the condition in which the samples received at our Laboratory.
- Reports cannot be used as on evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retain 30 one month from the date of sampling.

CORPORATE & Green Empire (Anupstgam), Above AXIS Bank, W. Vashi Complex Golf Main Road, Vadodra - 390 001 (Gujarat) INDIA.  
R & D TEL: +91 - 265 - 27 1269 Cell: +91 97 283 33635 Email: info@greencircleinc.com Website: W1-W3 Greencircleinc.com

	<b>Environment Clearance Compliance Report</b>		
Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

**Annexure – 07:** Good condition Vehicle used at site for bringing construction material and vehicle conform to pollution check certificate and applicable air and noise emission standards.

**Pollution Under Control Certificate** [See rules 115 (2)]  
 Authorised By: Government of Maharashtra

Date: 21/05/2023  
 Time: 18:11:27 PM  
 Validity upto: 20/11/2023

Certificate No. MH0500120011475  
 Registration No. MH04DW0477  
 Date of Registration 27/Nov/2018  
 Model & Year of Manufacturing 2018  
 Vehicle Model Number BHARAT STAGE III  
 Emission Norms DIESEL  
 Fuel MH050012  
 PUC Code No. 190010  
 GSTN No. 27A01000000000  
 Fee (GST to be paid extra as applicable) No.

Vehicle Photo with Registration plate 60 mm x 30 mm  
 MH.04.DW.0477

Sr. No.	Pollutant (as applicable)	Units (as applicable)	Emission limits	Measured Value (upto 2 decimal places)
1	Carbon Monoxide (CO)	percentage (%)		
	Hydrocarbon, (THC/HC)	ppm		
2	CO	percentage (%)		
	High idling emissions RPM	RPM	2500 ± 200	
3	Lambda		1 ± 0.03	
	Smoke Density Light absorption coefficient	1/metre	2.45	0.14

This PUC certificate is system generated through the national register of motor vehicles and does not require any signature.

Note: 1. Vehicle owners to link their mobile numbers to registered vehicle by logging to <https://puc.parivahan.gov.in>

Authorised Signature with stamp of PUC operator  
 60mm x 20 mm

**ROSHAN AUTO CARE**  
 Near Purnima Talkies,  
 Murbad Road, Kalyan (W).

THE GOVERNMENT OF INDIA  
**MAHARASHTRA STATE MOTOR DRIVING LICENCE**

DL No MH05 20080037963 DOI 01-06-1998  
 Valid Till 31-05-2018 (NT)

DLD 17-10-2016  
 FORM 7  
 RULE 19 (2)

AUTHORISATION TO DRIVE FOLLOWING CLASS OF VEHICLES THROUGHOUT INDIA  
 COV DOI  
 LMV 01-06-1998

DOB : 24-04-1980 BG AB+

Name RAHUL WANI  
 S/DW of RAJAN WANI  
 Add DEEPIKA APT, BK. NO-3, USHA NGR,  
 MURBAD RD, KALYAN (W).

PIN :  
 Signature & ID of Issuing Authority: MH05 2016167

Signature/Thumb impression of Holder

Project

Vashi Truck Terminal (VTT)

Date

10.06.2023

**Annexure – 8:** Ambient air and noise quality testing is being followed at site.

**GREEN CIRCLE, INC.**  
Integrated HSEOR Consulting Engineers, Scientists & Trainers  
(Recognized By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986)  
No. D - 1508 / 32 / 2007 - CPW  
(ISO 9001, 14001 & OHSAS 18001 Certified Organization)

Report No.: GC1/V/LAB/94-G01/23, SP/23 April-00/013 Date: 08/04/23


**ANALYSIS REPORT**

Client Details		Sample Details	
Name	M/s. Capacit'e Infraprojects Limited	Sample Code	GC1/V/23/CI/UC/2/AB11
Address	CECOO - Vashi Truck Terminal, Near AFMC Market, Sector - 19, Vashi Near Mumbai - 400703	Location	Tower - 10 & HTA AREA
Sampling Done By	Mr. Yasham	Quantity	N/A
Date of Sampling	03/04/23	Instruments	Respirable Dust Sampler & Fine Particulate Sampler
Sample Received Date	05/04/23	Sampling Method	IS 5182 - Part 5 - 1975
Date of Analysis	05/04/23	Date of Completion	06/04/23

**AMBIENT AIR ANALYSIS RESULTS**

Sr. No.	Parameters	Unit	Result	National Ambient Air Quality Standards	Reference Method
1.	Particulate Matter (PM <sub>10</sub> )	µg/m <sup>3</sup>	56.9	100	IS 5182 - Part 23: 2006
2.	Particulate Matter (PM <sub>2.5</sub> )	µg/m <sup>3</sup>	32.4	40	NAAQS Guidelines
3.	Sulphur dioxide (SO <sub>2</sub> )	µg/m <sup>3</sup>	23.3	80	IS 5182 - Part 2: 2001
4.	Oxides of Nitrogen (NO <sub>x</sub> )	µg/m <sup>3</sup>	23.8	80	IS 5182 - Part 4: 2006
5.	Carbon Monoxide (CO)	Mg/m <sup>3</sup>	0.39	2.0	IS 5182 - Part 10: 1999
6.	Ozone as O <sub>3</sub>	µg/m <sup>3</sup>	BDL	100	NAAQS Guidelines
7.	Amoniaq as NH <sub>3</sub>	µg/m <sup>3</sup>	109.8	400	NAAQS Guidelines
8.	Lead as Pb	µg/m <sup>3</sup>	BDL	1.0	NAAQS Guidelines
9.	Nickel as Ni	µg/m <sup>3</sup>	BDL	20	NAAQS Guidelines
10.	Arsenic as As	µg/m <sup>3</sup>	BDL	4.0	NAAQS Guidelines
11.	Benzene - C <sub>6</sub> H <sub>6</sub>	µg/m <sup>3</sup>	BDL	5.0	IS 5182(Part 11): 2006
12.	Benzol (a) Pyrene	µg/m <sup>3</sup>	BDL	1.0	Gas Chromatography


Remark: Results are within limit as per Maharashtra Pollution Control Board.

  
Authorized Signatory





- Analysis is subject to the condition in which the sample is received at our Laboratory.
- Report's cannot be used as an evidence anywhere including judicialy purpose without our prior permission.
- Sample will be retained till one month from the date of sampling.

CORP. OFFICE S & R D: Green Empire (Anushakti), Above Axis Bank, Nr. Yash Complex, Octal Main Road Vadodra 390021(Gujarat) INDIA.  
Tel.: 91-269-2371259 Cell: + 919226583625 Email: info@greencircleinc.com Website: www.greencircleinc.com



<b>CAPACIT'E</b> INFRAPROJECTS LIMITED 	<b>Environment Clearance Compliance Report</b>		<b>TATA CONSULTING ENGINEERS LIMITED</b> TATA Consulting Engineers Ltd. - Hiten Sethi & Associates JV <b>HSA</b> HSA CONSULTING ENGINEERS LIMITED TATA Consulting Engineers Ltd. - Hiten Sethi & Associates JV
Project	Vashi Truck Terminal (VTT)	Date	10.06.2023

**Annexure - 09:** Curing Compound used to reduce the water demand during construction.

	 <small>TATA Consulting Engineers Ltd. - Hiten Sethi &amp; Associates JV</small>	 <small>HSA CONSULTING ENGINEERS LIMITED</small>	 <small>WE MAKE CITIES</small>
<b>METHOD STATEMENT</b>		Doc No: MST-CIL CIDCO/42	
CIDCO PMAY PACKAGE II PROJECTS		Rev-R0 Date of Rev: 5/05/2022	

**METHOD STATEMENT  
FOR APPLICATION OF CURING COMPOUND TO RCC MEMBERS**

[ Make: SIKA BRAND]

Project name- "Construction of EWS/LIG type dwelling units (Package II), CIDCO"  
Contract number- C.A.No.: 01/CIDCO/CE(SP)/2019-20  
Client- CIDCO  
PMC- TCE-HSA JV  
Contractor - CAPACIT'E INFRAPROJECT LTD

	Prepared by	Reviewed by	Reviewed by	Approved by
	CIL	CIL	PMC	CIDCO
NAME	Arun Giriyan	Sunil Wagh	Ashok Salvi	
DESIGNATION	AVP-QA/QC	SR.PRESIDENT	PROJECT MANAGER	
SIGN				





Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

**Annexure – 10** : Noise Level Monitoring is being followed at site.



Sl. No.	Location / Area	Noise Level	Remarks
1	Tower No:- 07	68 db	ok
2	Tower No:- 08	71 db	ok
3	Tower No:- 09	70 db	ok
4	M.T.A. Area / Steel Yard	65 db	ok
5	Tower no 11B12	64 db	ok
6	M.T.A. Area	70 db	ok
7	Labour Camp	70 db	ok
8	Behind Labour Camp	65 db	ok
9	Steel Area	71 db	ok
10	MINOR Fabrication Area	71 db	ok
11	Office Area	68 db	ok
12	Tower no:- 01	70 db	ok
13	Tower no:- 03	70 db	ok
14	Tower no:- 02	65 db	ok
15	Tower no:- 05	70 db	ok

Location in charge/ Supervisor:  
Name and Signature: *[Signature]*  
Review by Site In Charge:


Safety Person: Adish  
Name and Signature: *[Signature]*



Noise Level Measuring is being followed during night work to comply the applicable rules and regulation.

Project	Vashi Truck Terminal (VTT)	Date	10.06.2023
---------	----------------------------	------	------------

**Annexure – 11:** Vehicle parked only inside of project.

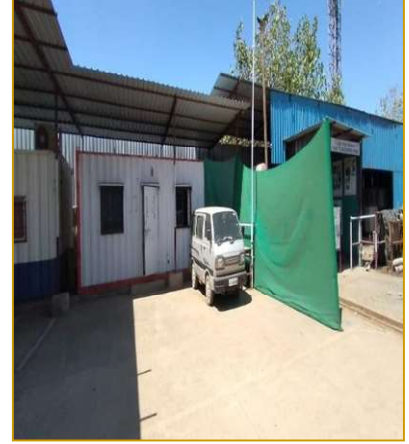

\*\*\*\*\*
